
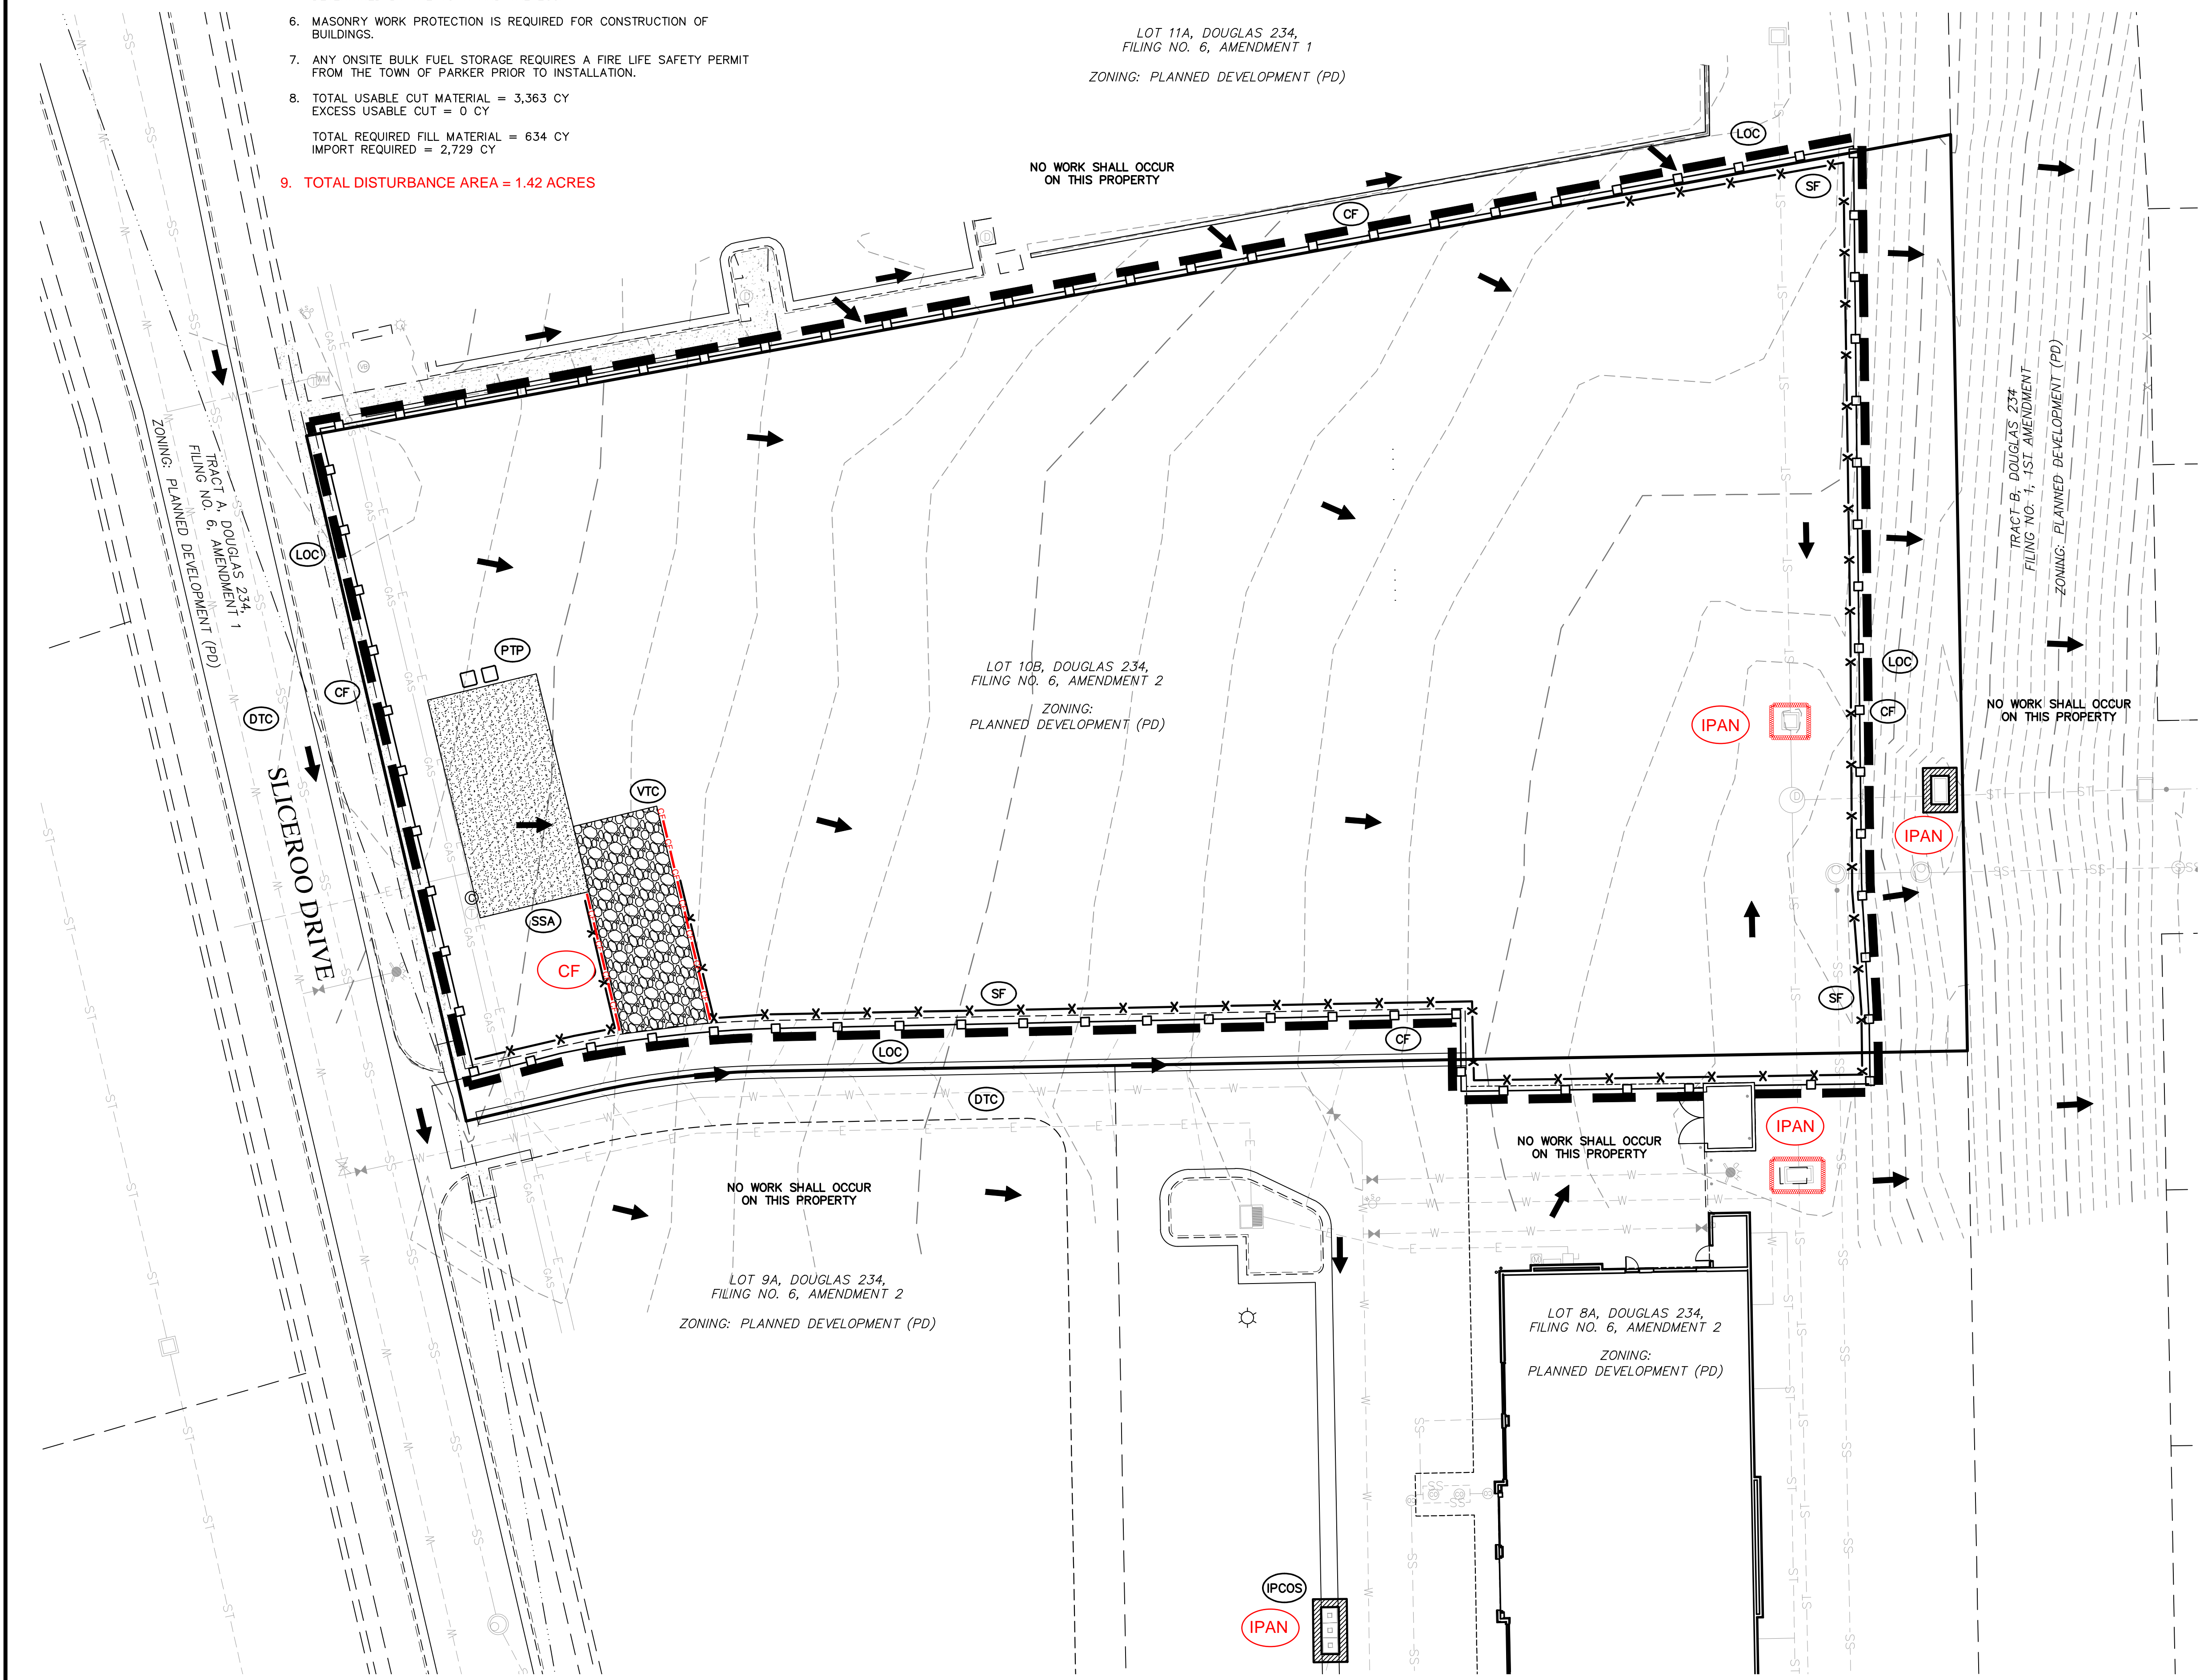


NOTES

1. THE DISTURBED AREA IS 1.5 ACRES.
2. THE VTC PAD FOR A CWA DOES NOT NEED TO CONFORM TO THE FORMAL VTC DETAIL.
3. THE TRUE LOCATION OF THE CWA MAY BE DETERMINED BY THE TOWN AND THE ECS.
4. LOT PROTECTION (LP) IS REQUIRED ON COMMERCIAL LOTS WHEN COMPLETION OF LANDSCAPING IS NOT POSSIBLE AND PRIOR TO ISSUANCE OF A TEMPORARY CERTIFICATE OF OCCUPANCY.
5. THE TRUE LOCATION OF THE PORTABLE TOILET PROTECTION (PTP) MAY BE DETERMINED BY THE TOWN AND THE ECS.
6. MASONRY WORK PROTECTION IS REQUIRED FOR CONSTRUCTION OF BUILDINGS.
7. ANY ONSITE BULK FUEL STORAGE REQUIRES A FIRE LIFE SAFETY PERMIT FROM THE TOWN OF PARKER PRIOR TO INSTALLATION.
8. TOTAL USABLE CUT MATERIAL = 3,363 CY
EXCESS USABLE CUT = 0 CY
TOTAL REQUIRED FILL MATERIAL = 634 CY
IMPORT REQUIRED = 2,729 CY
9. TOTAL DISTURBANCE AREA = 1.42 ACRES

EROSION CONTROL MEASURE SUMMARY TABLE

	SILT FENCE	STABILIZED STAGING AREA	CONCRETE WASHOUT AREA	VEHICLE TRACKING CONTROL	INLET PROTECTION	EROSION CONTROL BLANKET	SEEDING & MULCHING	PORTABLE TOILET PROTECTION	DEBRIS AND TRASH CONTROL	SEDIMENT CONTROL LOG	CONSTRUCTION FENCE
INITIAL CONDITION	659 LF	150 SY	0	1 EA	2 EA	0	0	1 EA	1 EA	0	1,075 LF

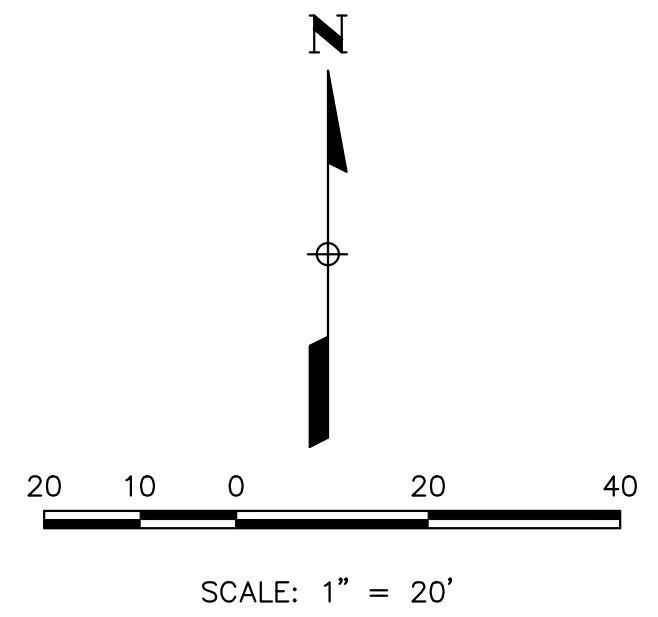

LEGEND

- PROPERTY LINE
- - - EXISTING CONTOUR
- - - PROPOSED CONTOUR
- DRAINAGE FLOW DIRECTION
- EXISTING CURB & GUTTER
- PROPOSED 1' SPILL CURB & GUTTER
- PROPOSED 2' CATCH CURB & GUTTER
- - - PROPOSED EASEMENT
- - - EXISTING EASEMENT
- - - EXISTING SANITARY SEWER
- - - EXISTING WATERLINE
- - - EXISTING GAS PIPE
- - - EXISTING UNDERGROUND ELECTRIC
- - - EXISTING STORM SEWER
- ⊗ CD CHECK DAM
- ⊗ CB COMPOST BLANKET
- ⊗ CFB COMPOST FILTER BERM
- ⊗ CWA CONCRETE WASHOUT AREA
- ⊗ CF CONSTRUCTION FENCE
- ⊗ CM CONSTRUCTION MARKER
- ⊗ DW DEWATERING
- ⊗ DD DIVERSION DITCH
- ⊗ ECB EROSION CONTROL BLANKET (STRAW-COCOONUT)
- ⊗ GMS GROUT MIXING STATION
- ⊗ IP INLET PROTECTION
- ⊗ RCD REINFORCED CHECK DAM
- ⊗ RRB REINFORCED ROCK BERM
- ⊗ RRC RRB FOR CULVERT PROTECTION
- ⊗ SB SEDIMENT BASIN
- ⊗ SCL SEDIMENT CONTROL LOG
- ⊗ SS STREET SWEEPING
- ⊗ ST SEDIMENT TRAP
- ⊗ SM SEEDING AND MULCHING
- ⊗ SF SILT FENCE
- ⊗ SSA STABILIZED STAGING AREA
- ⊗ SR SURFACE ROUGHENING
- ⊗ TSD TEMPORARY SLOPE DRAIN
- ⊗ TSC TEMPORARY STREAM CROSSING
- ⊗ TER TERRACING
- ⊗ VTC VEHICLE TRACKING CONTROL
- ⊗ VTC WITH WHEEL WASH
- ⊗ LOC LIMITS OF CONSTRUCTION
- ⊗ RS ROCK SOCKS
- ⊗ PTP POTABLE TOILET PROTECTION
- ⊗ DTC DEBRIS AND TRASH CONTROL

BENCHMARK

BENCHMARK IS BY GPS OBSERVATION NAVD 88. SITE BENCHMARK AT NORTHWEST CORNER OF INLET ON CHAMBERS RD. APPROXIMATELY 200' +/- NORTH OF HESS RD.

ENGINEER'S STATEMENT

PREPARED UNDER MY SUPERVISION

BRIAN KROMBEIN, PE, PLS
COLORADO PE NO. 34294
FOR AND ON BEHALF OF
VERMILION PEAK ENGINEERING LLC



UNTIL SUCH TIME AS THESE DRAWINGS ARE APPROVED BY THE APPROPRIATE AGENCIES, VERMILION PEAK ENGINEERING APPROVES THEIR USE ONLY FOR THE PURPOSES DESIGNATED BY WRITTEN AUTHORIZATION.

PREPARED FOR
VENTANA CAPITAL
8678 CONCORD CENTER DR, SUITE 200
ENGLEWOOD, CO 80112
720-703-9036
CONTACT: DALTON HORAN





DATE	BY	REVISION

NOTES

1. THE DISTURBED AREA IS 1.5 ACRES.
2. THE VTC PAD FOR A CWA DOES NOT NEED TO CONFORM TO THE FORMAL VTC DETAIL.
3. THE TRUE LOCATION OF THE CWA MAY BE DETERMINED BY THE TOWN AND THE ECS.
4. LOT PROTECTION (LP) IS REQUIRED ON COMMERCIAL LOTS WHEN COMPLETION OF LANDSCAPING IS NOT POSSIBLE AND PRIOR TO ISSUANCE OF A TEMPORARY CERTIFICATE OF OCCUPANCY.
5. THE TRUE LOCATION OF THE PORTABLE TOILET PROTECTION (PTP) MAY BE DETERMINED BY THE TOWN AND THE ECS.
6. MASONRY WORK PROTECTION IS REQUIRED FOR CONSTRUCTION OF BUILDINGS.
7. ANY ONSITE BULK FUEL STORAGE REQUIRES A FIRE LIFE SAFETY PERMIT FROM THE TOWN OF PARKER PRIOR TO INSTALLATION.
8. TOTAL USABLE CUT MATERIAL = 3,363 CY
EXCESS USABLE CUT = 0 CY
TOTAL REQUIRED FILL MATERIAL = 634 CY
IMPORT REQUIRED = 2,729 CY
9. TOTAL DISTURBANCE AREA = 1.42 ACRES

EROSION CONTROL MEASURE SUMMARY TABLE

	SILT FENCE	STABILIZED STAGING AREA	CONCRETE WASHOUT AREA	VEHICLE TRACKING CONTROL	INLET PROTECTION	EROSION CONTROL BLANKET	SEEDING & MULCHING	PORTABLE TOILET PROTECTION	DEBRIS AND TRASH CONTROL	SEDIMENT CONTROL LOG	CONSTRUCTION FENCE	SURFACE ROUGHENING
INTERIM CONDITION	0	0	1 EA	0	2 EA	167 SY	0	0	1 EA	496 LF	0	0.5 AC.

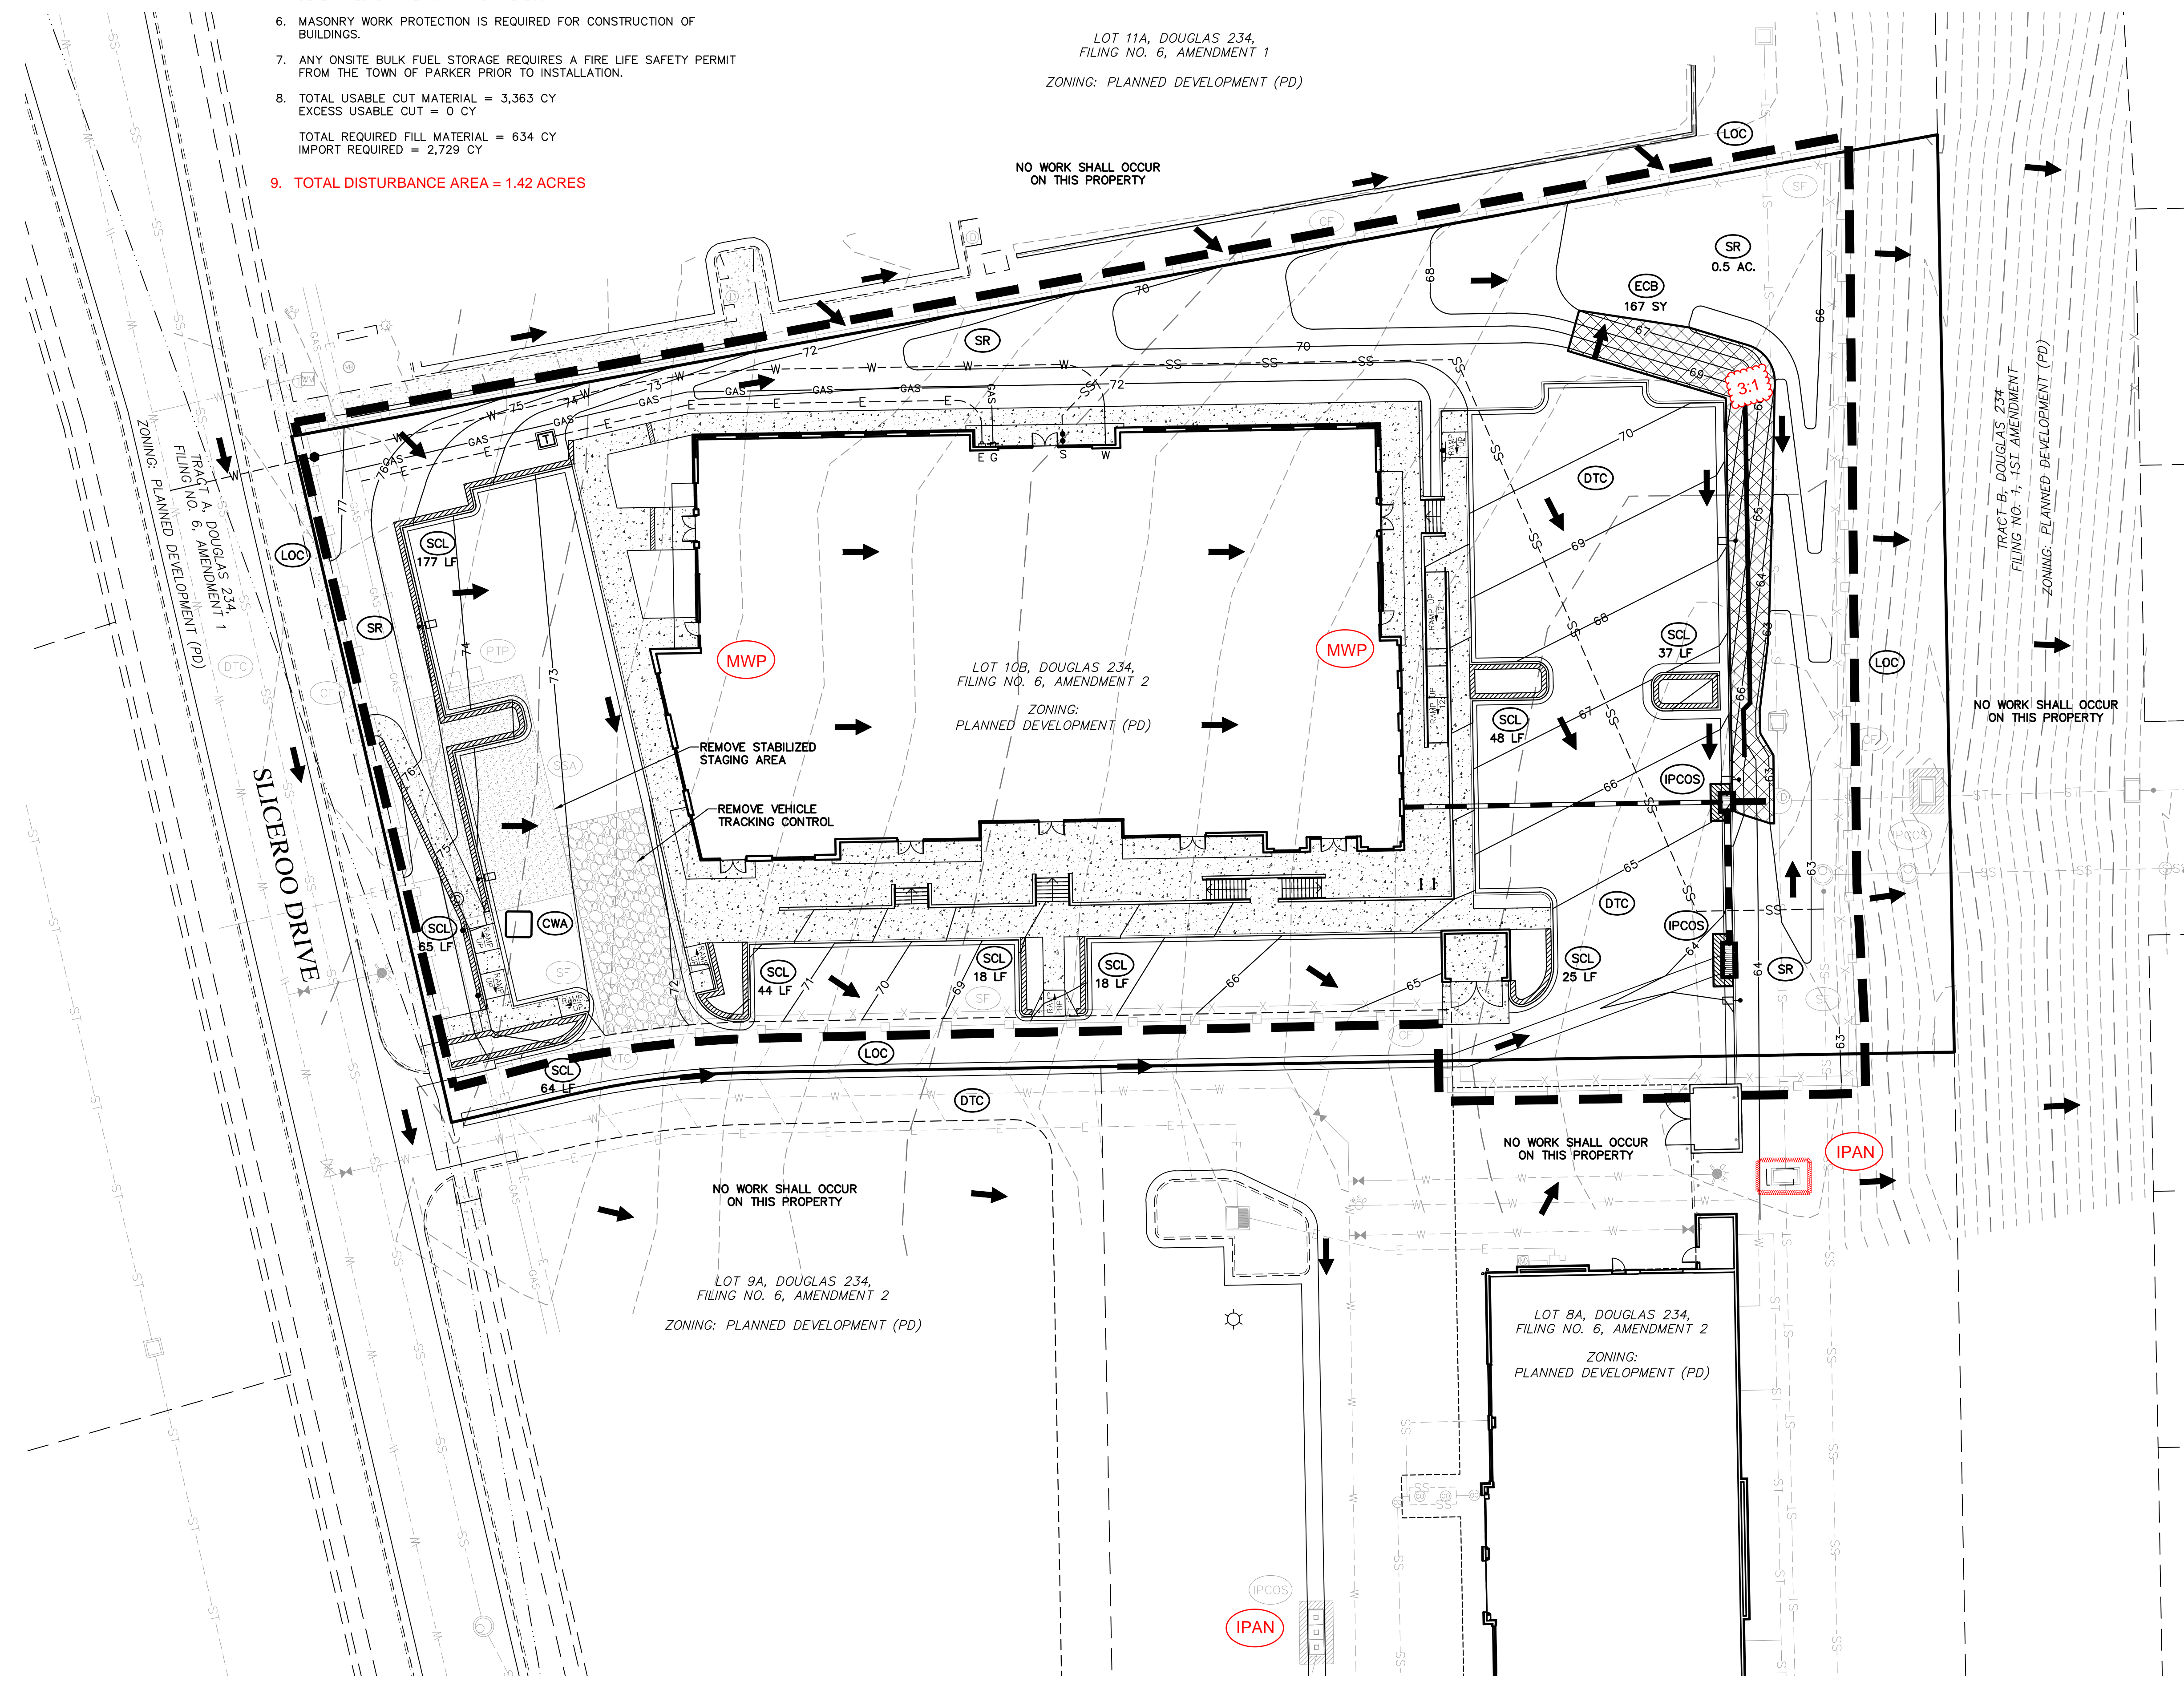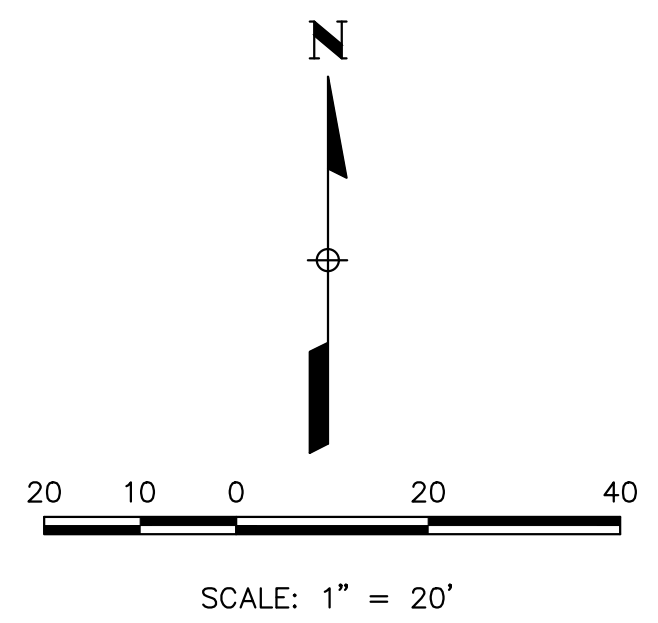

LEGEND

- PROPERTY LINE
- - - EXISTING CONTOUR
- - - PROPOSED CONTOUR
- DRAINAGE FLOW DIRECTION
- EXISTING CURB & GUTTER
- PROPOSED 1' SPILL CURB & GUTTER
- PROPOSED 2' CATCH CURB & GUTTER
- - - PROPOSED EASEMENT
- - - EXISTING EASEMENT
- - - EXISTING SANITARY SEWER
- - - EXISTING WATERLINE
- - - EXISTING GAS PIPE
- - - EXISTING UNDERGROUND ELECTRIC
- - - EXISTING STORM SEWER
- ⊠ CD CHECK DAM
- ⊠ CB COMPOST BLANKET
- ⊠ CFB COMPOST FILTER BERM
- ⊠ CWA CONCRETE WASHOUT AREA
- ⊠ CF CONSTRUCTION FENCE
- ⊠ CM CONSTRUCTION MARKER
- ⊠ DW DEWATERING
- ⊠ DD DIVERSION DITCH
- ⊠ ECB EROSION CONTROL BLANKET (STRAW-COCOONUT)
- ⊠ GMS GROUT MIXING STATION
- ⊠ IP INLET PROTECTION
- ⊠ RCD REINFORCED CHECK DAM
- ⊠ RRB REINFORCED ROCK BERM
- ⊠ RRC RRB FOR CULVERT PROTECTION
- ⊠ SB SEDIMENT BASIN
- ⊠ SCL SEDIMENT CONTROL LOG
- ⊠ SS STREET SWEEPING
- ⊠ ST SEDIMENT TRAP
- ⊠ SM SEEDING AND MULCHING
- ⊠ SF SILT FENCE
- ⊠ SSA STABILIZED STAGING AREA
- ⊠ SR SURFACE ROUGHENING
- ⊠ TSD TEMPORARY SLOPE DRAIN
- ⊠ TSC TEMPORARY STREAM CROSSING
- ⊠ TER TERRACING
- ⊠ VTC VEHICLE TRACKING CONTROL
- ⊠ WW VTC WITH WHEEL WASH
- ⊠ LOC LIMITS OF CONSTRUCTION
- ⊠ RS ROCK SOCKS
- ⊠ PTP PORTABLE TOILET PROTECTION
- ⊠ DTC DEBRIS AND TRASH CONTROL

BENCHMARK

BENCHMARK IS BY GPS OBSERVATION NAVD 88. SITE BENCHMARK AT NORTHWEST CORNER OF INLET ON CHAMBERS RD. APPROXIMATELY 200' +/- NORTH OF HESS RD.

ENGINEER'S STATEMENT

PREPARED UNDER MY SUPERVISION

BRIAN KROMBEIN, PE, PLS
COLORADO PE NO. 34294
DATE
FOR AND ON BEHALF OF
VERMILION PEAK ENGINEERING LLC



UNTIL SUCH TIME AS THESE DRAWINGS ARE APPROVED BY THE APPROPRIATE AGENCIES, VERMILION PEAK ENGINEERING APPROVES THEIR USE ONLY FOR THE PURPOSES DESIGNATED BY WRITTEN AUTHORIZATION.

PREPARED FOR
VENTANA CAPITAL
8678 CONCORD CENTER DR, SUITE 200
ENGLEWOOD, CO 80112
720-703-9036
CONTACT: DALTON HORAN



No.	REVISION	DATE	BY
1		2/12/25	BK
2			BK
3			BK


HORSE CREEK COMMERCIAL
INTERIM
EROSION CONTROL PLAN

NOTES

1. THE DISTURBED AREA IS 1.5 ACRES.
2. THE VTC PAD FOR A CWA DOES NOT NEED TO CONFORM TO THE FORMAL VTC DETAIL.
3. THE TRUE LOCATION OF THE CWA MAY BE DETERMINED BY THE TOWN AND THE ECS.
4. LOT PROTECTION (LP) IS REQUIRED ON COMMERCIAL LOTS WHEN COMPLETION OF LANDSCAPING IS NOT POSSIBLE AND PRIOR TO ISSUANCE OF A TEMPORARY CERTIFICATE OF OCCUPANCY.
5. THE TRUE LOCATION OF THE PORTABLE TOILET PROTECTION (PTP) MAY BE DETERMINED BY THE TOWN AND THE ECS.
6. MASONRY WORK PROTECTION IS REQUIRED FOR CONSTRUCTION OF BUILDINGS.
7. ANY ONSITE BULK FUEL STORAGE REQUIRES A FIRE LIFE SAFETY PERMIT FROM THE TOWN OF PARKER PRIOR TO INSTALLATION.
8. TOTAL USABLE CUT MATERIAL = 3,363 CY
EXCESS USABLE CUT = 0 CY
TOTAL REQUIRED FILL MATERIAL = 634 CY
IMPORT REQUIRED = 2,729 CY
9. **TOTAL DISTURBANCE AREA = 1.42 ACRES**

EROSION CONTROL MEASURE SUMMARY TABLE

	SILT FENCE	STABILIZED STAGING AREA	CONCRETE WASHOUT AREA	VEHICLE TRACKING CONTROL	INLET PROTECTION	EROSION CONTROL BLANKET	SEEDING & MULCHING	PORTABLE TOILET PROTECTION	DEBRIS AND TRASH CONTROL	SEDIMENT CONTROL LOG	CONSTRUCTION FENCE
FINAL CONDITION	0	0	0	0	0	0	0.5 AC.	0	1 EA	0	0

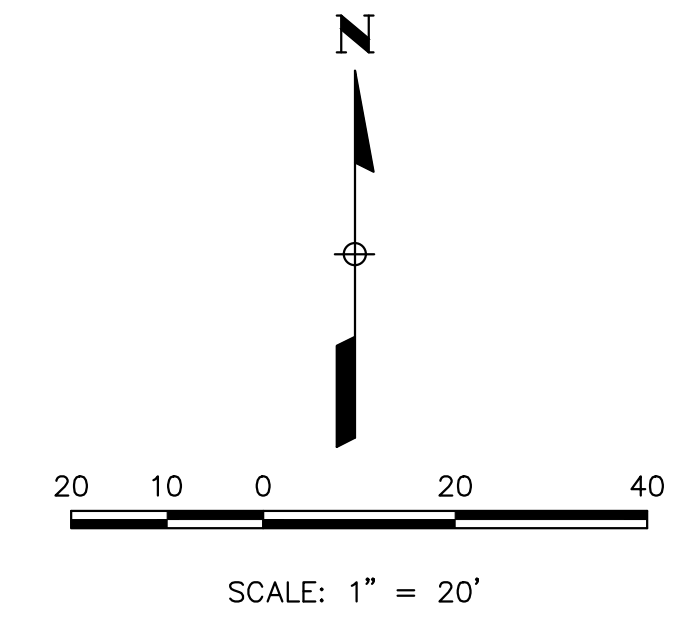

LOT 11A, DOUGLAS 234,
FILING NO. 6, AMENDMENT 1
ZONING: PLANNED DEVELOPMENT (PD)

NO WORK SHALL OCCUR
ON THIS PROPERTY

LOT 10B, DOUGLAS 234,
FILING NO. 6, AMENDMENT 2
ZONING: PLANNED DEVELOPMENT (PD)

LOT 9A, DOUGLAS 234,
FILING NO. 6, AMENDMENT 2
ZONING: PLANNED DEVELOPMENT (PD)

LOT 8A, DOUGLAS 234,
FILING NO. 6, AMENDMENT 2
ZONING: PLANNED DEVELOPMENT (PD)

Add Parker's COMPLETE List of Keys/Symbols (1st), General Notes (2nd), and Erosion Control Details in ALPHABETICAL Order (3rd), Immediately Following the Final Erosion Control Plan Sheet.

LEGEND

- PROPERTY LINE
- - - EXISTING CONTOUR
- - - PROPOSED CONTOUR
- DRAINAGE FLOW DIRECTION
- EXISTING CURB & GUTTER
- PROPOSED 1' SPILL CURB & GUTTER
- PROPOSED 2' CATCH CURB & GUTTER
- - - PROPOSED EASEMENT
- - - EXISTING EASEMENT
- - - EXISTING SANITARY SEWER
- - - EXISTING WATERLINE
- - - EXISTING GAS PIPE
- - - EXISTING UNDERGROUND ELECTRIC
- - - EXISTING STORM SEWER
- ⊘ CD CHECK DAM
- ⊘ CB COMPOST BLANKET
- ⊘ CFB COMPOST FILTER BERM
- ⊘ CWA CONCRETE WASHOUT AREA
- ⊘ CF CONSTRUCTION FENCE
- ⊘ CM CONSTRUCTION MARKER
- ⊘ DW DEWATERING
- ⊘ DD DIVERSION DITCH
- ⊘ ECB EROSION CONTROL BLANKET (STRAW-COCONUT)
- ⊘ GMS GROUT MIXING STATION
- ⊘ IP INLET PROTECTION
- ⊘ RCD REINFORCED CHECK DAM
- ⊘ RRB REINFORCED ROCK BERM
- ⊘ RRC RRB FOR CULVERT PROTECTION
- ⊘ SB SEDIMENT BASIN
- ⊘ SCL SEDIMENT CONTROL LOG
- ⊘ SS STREET SWEEPING
- ⊘ ST SEDIMENT TRAP
- ⊘ SM SEEDING AND MULCHING
- ⊘ SF SILT FENCE
- ⊘ SSA STABILIZED STAGING AREA
- ⊘ SR SURFACE ROUGHENING
- ⊘ TSD TEMPORARY SLOPE DRAIN
- ⊘ TSC TEMPORARY STREAM CROSSING
- ⊘ TER TERRACING
- ⊘ VTC VEHICLE TRACKING CONTROL
- ⊘ WW VTC WITH WHEEL WASH
- ⊘ LOC LIMITS OF CONSTRUCTION
- ⊘ RS ROCK SOCKS
- ⊘ PTP PORTABLE TOILET PROTECTION
- ⊘ DTC DEBRIS AND TRASH CONTROL


BENCHMARK

BENCHMARK IS BY GPS OBSERVATION NAVD 88. SITE BENCHMARK AT NORTHWEST CORNER OF INLET ON CHAMBERS RD. APPROXIMATELY 200' +/- NORTH OF HESS RD.

ENGINEER'S STATEMENT


PREPARED UNDER MY SUPERVISION

BRIAN KROMBEIN, PE, PLS DATE
COLORADO PE NO. 34294
FOR AND ON BEHALF OF
VERMILION PEAK ENGINEERING LLC



UNTIL SUCH TIME AS THESE DRAWINGS ARE APPROVED BY THE APPROPRIATE VERMILION PEAK ENGINEERING APPROVES THEIR USE ONLY FOR THE PURPOSES DESIGNATED BY WRITTEN AUTHORIZATION.

PREPARED FOR
VENTANA CAPITAL
8678 CONCORD CENTER DR, SUITE 200
ENGLEWOOD, CO 80112
720-703-9036
CONTACT: DALTON HORAN



No.	REVISION	DATE	BY

HORSE CREEK COMMERCIAL
FINAL
EROSION CONTROL PLAN

1. GRADING, DRILLING, CLEARING, EXCAVATING, BACK-FILLING, SOIL STRIPPING, SOIL IMPORTING EXPORTING OR ANY OTHER FORM OF SOIL DISTURBANCE SHALL NOT COMMENCE UNTIL A TOWN OF PARKER GRADING/EXCAVATION PERMIT HAS BEEN ISSUED.
2. THE TOWN OF PARKER GRADING/EXCAVATION PERMIT IS VALID FOR A PERIOD OF 2 YEARS FROM THE DATE OF ISSUANCE. ANY LAPSE IN PERMIT COVERAGE MAY RESULT IN THE ISSUANCE OF A STOP WORK ORDER AND/OR FINES.
3. ALL EROSION AND SEDIMENT CONTROL BMPs SHALL BE INSTALLED ACCORDING TO THE CBMP PLAN INSTALLATION NOTES AND DETAILS AND/OR PERMITTED VARIANCES. ALL MATERIALS, WORKMANSHIP AND INSTALLATION METHODS ARE SUBJECT TO INSPECTION BY THE TOWN'S INSPECTOR. THE TOWN OF PARKER RESERVES THE RIGHT TO ACCEPT OR REJECT ANY SUCH MATERIALS, WORKMANSHIP AND/OR INSTALLATION METHODS THAT DO NOT CONFORM TO THE CBMP PLAN AND/OR PERMITTED VARIANCES.
4. THE EROSION CONTROL SUPERVISOR SHALL REVISE OR MODIFY THE EROSION AND SEDIMENT CONTROL MEASURES IF IT BECOMES APPARENT THAT THE ORIGINAL PLAN IS INADEQUATE, OR AS A RESULT OF DEFICIENCIES IDENTIFIED DURING INSPECTIONS PERFORMED BY THE TOWN'S INSPECTOR.
5. THE INSTALLATION OF ADDITIONAL EROSION AND SEDIMENT CONTROL BEST MANAGEMENT PRACTICES (BMPs) MAY BE REQUIRED OF THE EROSION CONTROL SUPERVISOR, PROPERTY OWNER, SITE DEVELOPER, CONTRACTOR AND/OR THEIR AUTHORIZED AGENTS AT ANY TIME THROUGHOUT THE DURATION OF THE PROJECT CONSTRUCTION AND/OR SUBSEQUENT REVEGETATION PERIOD.
6. THE EROSION CONTROL SUPERVISOR SHALL BE RESPONSIBLE FOR ENSURING THAT THE SITE REMAINS IN COMPLIANCE WITH THE NOTICE OF NUISANCE REPORTS (a.k.a., CONSTRUCTION SITE RUNOFF CONTROL INSPECTION REPORTS), APPROVED CBMP PLAN(S) AND THE TOWN OF PARKER STORM DRAINAGE AND ENVIRONMENTAL CRITERIA MANUAL.
7. THE EROSION CONTROL SUPERVISOR SHALL BE REMAIN AVAILABLE TO DISCUSS AND CORRECT ANY PROBLEMS THAT MAY ARISE RELATING TO GRADING, EROSION AND SEDIMENT CONTROL.
8. IF IT IS ANTICIPATED THAT ALL OR A PORTION OF THE PROJECT WILL OCCUR DURING SEASONS SUSCEPTIBLE TO SNOWFALL, THE USE OF CERTAIN EROSION AND SEDIMENT CONTROL BMPs ADJACENT TO PUBLIC ROADWAYS MAY NEED TO BE RECONSIDERED DUE TO THE NATURE OF SNOW REMOVAL OPERATIONS. AN APPROVED ALTERNATIVE MAY BE NECESSARY TO MINIMIZE DAMAGE FROM THESE OPERATIONS. THE TOWN OF PARKER ASSUMES NO RESPONSIBILITY FOR DAMAGE TO ANY BMPs AS A RESULT OF SNOW FLOWING AND SNOW REMOVAL.
9. AREAS OF LAND DISTURBANCE EQUAL TO 40 ACRES OR GREATER SHALL NOT BE EXPOSED FOR MORE THAN 30 CONSECUTIVE DAYS WITHOUT TEMPORARY OR PERMANENT STABILIZATION.
10. AUTHORIZED EXEMPTIONS MAY BE ALLOWED TO THE 40-ACRE LIMIT FOR REMOVAL AND STORAGE OF CUT MATERIAL WHERE (A) GEOTECHNICAL LIMITATIONS RESTRICT THE USE OF TEMPORARY OR PERMANENT STABILIZATION OF THE STORED MATERIAL (E.G., SHELING SOILS ROCK) AND (B) WHEN THE OWNER CAN DEMONSTRATE THAT THE 40-ACRE LIMIT IS PHYSICALLY AND/OR FINANCIALLY IMPRACTICABLE. FOR SITES GRANTED THIS EXEMPTION, A PHASING AND EARTHWORK QUANTITIES PLAN SHALL BE SUBMITTED TO THE PUBLIC WORKS DEPARTMENT AND APPROVED PRIOR TO THE COMMENCEMENT OF LAND DISTURBANCE ACTIVITIES. SUBMITTAL REQUIREMENTS INCLUDE:
 - (i) PHASING PLAN SHOWING CUT AND FILL VOLUMES AND LOCATIONS FOR EACH PHASE AND PROJECT TOTALS.
 - (ii) EARTHWORK QUANTITY PLAN SHOWING CUT AND FILL VOLUMES AND LOCATIONS FOR EACH PHASE AND PROJECT TOTALS.
 - (iii) BMP PLAN SHOWING SPECIFIC EROSION AND SEDIMENT CONTROLS FOR EACH PHASE.

CBMP CONSTRUCTION BEST MANAGEMENT PRACTICES
 GEN NOTES 1 OF 4
 Oct. 2013

- LP LOT PROTECTION
- MWP MASONRY WORK PROTECTION
- PTP PORTABLE TOILET PROTECTION
- RCSC ROUGH CUT STREET CONTROL
- RS ROCK SOCK
- RSS ROCK SOCK IN SWALE
- SB STRAW BALE
- SCL SEDIMENT CONTROL LOGS
- SF SILT FENCE
- SMC SEEDING, MULCHING AND CRIMPING
- SR SURFACE ROUGHING
- SSA STABILIZED STAGING AREA
- STP SIDEWALK TRANSITION PROTECTION

CBMP CONSTRUCTION BEST MANAGEMENT PRACTICES
 LEGEND 2 OF 3
 Oct. 2013

11. ANY EROSION AND SEDIMENT CONTROL BMPs THAT ARE DAMAGED OR IN NEED OF MAINTENANCE OR REPLACEMENT SHALL BE CORRECTED AS SOON AS POSSIBLE, IMMEDIATELY IN MOST CASES.
12. ALL DEFICIENCIES LISTED ON THE NOTICE OF NUISANCE FORM SHALL BE COMPLETED AS SOON AS POSSIBLE, IMMEDIATELY IN MOST CASES. ALL REQUIRED ACTIONS MUST BE IN THE CORRECTED FORM DURING THE FOLLOW-UP INSPECTION.
13. THE EROSION CONTROL SUPERVISOR IS RESPONSIBLE FOR ENSURING THAT ALL STREETS, CURBS, CUTTERS, SIDEWALKS, DRIVEWAYS, PARKING LOTS, ALLEYS, TRICKLE CHANNELS, AND/OR OTHER IMPERVIOUS SURFACES IMPACTED BY CONSTRUCTION ACTIVITIES ARE THOROUGHLY CLEANED THROUGHOUT THE DAY IF THEY BECOME SOILED. THESE AREAS MUST ALSO BE THOROUGHLY CLEAN BEFORE THE END OF THE WORK DAY.
14. BULK STORAGE STRUCTURES FOR PETROLEUM PRODUCTS AND OTHER CHEMICALS SHALL HAVE ADEQUATE PROTECTION SO AS TO CONTAIN ALL SPILLS AND PREVENT ANY SPILLED MATERIAL FROM ENTERING STATE WATERS.
15. ALL TRASH RECEPTACLES ON SITE SHALL BE FREE OF HOLES, CRACKS, GAPS, AND/OR OTHER PERMEABLE AREAS THAT MAY ALLOW FOR THE DISCHARGE OF POLLUTANTS.
16. ALL TRASH RECEPTACLES ON SITE SHALL BE EMPTIED AT A FREQUENCY AS TO ENSURE THAT THE TRASH REMAINS CONFINED TO THE RECEPTACLE.
17. ALL LOOSE TRASH AND LITTER ASSOCIATED WITH THE PROJECT MUST BE REMOVED AND PROPERLY DISCARDED ON A DAILY BASIS.
18. ALL PORTABLE TOILETS SHALL BE STAKED DOWN AT ALL TIMES USING U-SHAPED REBAR STAKES. THE PORTABLE TOILETS SHALL ALSO BE PLACED A MINIMUM DISTANCE OF 10 FEET FROM ALL IMPERVIOUS SURFACES, INCLUDING, BUT NOT LIMITED TO STREETS CURBS, CUTTERS, SIDEWALKS AND PARKING LOTS.
19. THE EROSION CONTROL SUPERVISOR SHALL MAINTAIN STRICT ADHERENCE TO THE LIMITS OF CONSTRUCTION AND PROPERTY LIMITS FOR ALL MATERIALS, VEHICLES AND EQUIPMENT. FAILURE TO ABIDE BY THIS REQUIREMENT MAY RESULT IN THE ISSUANCE OF A STOP WORK ORDER.
20. ALL CONSTRUCTION TRAFFIC MUST ENTER AND EXIT THE SITE THROUGH THE APPROVED ACCESS POINT(S). A VEHICLE TRACKING CONTROL PAD IS REQUIRED AT ALL APPROVED ACCESS POINTS TO THE SITE. EXCEPTIONS MAY BE CONSIDERED FOR CONSTRUCTION ACTIVITY OCCURRING IMMEDIATELY ADJACENT TO PAVED AREAS AND WHERE ALTERNATIVE BMPs ARE IMPLEMENTED. SUCH ACTIVITY MAY INCLUDE, BUT NOT BE LIMITED TO RESIDENTIAL, CONSTRUCTION, UTILITY CONSTRUCTION, ETC.
21. NO PERMANENT SLOPES GREATER THAN 3:1 ARE ALLOWED.
22. ALL PERMANENT SLOPES STEEPER THAN 4:1 (HORIZONTAL TO VERTICAL) SHALL REQUIRE EROSION CONTROL BLANKETS. TEMPORARY SLOPES IN TEMPORARY SEDIMENT BASINS THAT ARE STEEPER THAN 4:1 MAY REQUIRE EROSION CONTROL BLANKETS.
23. THE EROSION CONTROL SUPERVISOR SHALL BE RESPONSIBLE FOR CORRECTING ANY ADVERSE IMPACTS THAT OCCUR TO NEIGHBORING PROPERTIES. THE EROSION CONTROL SUPERVISOR MUST OBTAIN PERMISSION FROM LAND OWNERS PRIOR TO ENTERING SUCH PROPERTY.
24. A WATER SOURCE SHALL BE AVAILABLE ONSITE DURING CONSTRUCTION ACTIVITIES, AND UTILIZED TO MINIMIZE FUGITIVE DUST. ALTERNATIVE BMPs MAY BE REQUIRED IF INITIAL ATTEMPTS TO SUPPRESS DUST ARE UNSUCCESSFUL.


CBMP CONSTRUCTION BEST MANAGEMENT PRACTICES
 GEN NOTES 2 OF 4
 Oct. 2013

- TI TEMPORARY IRRIGATION
- TSB TEMPORARY SEDIMENT BASIN
- VTC VEHICLE TRACKING CONTROL

CBMP CONSTRUCTION BEST MANAGEMENT PRACTICES
 LEGEND 3 OF 3
 Oct. 2013

25. ALL CHEMICAL OR HAZARDOUS MATERIAL SPILLS, INCLUDING CONCRETE WASHOUT WATER, WHICH MAY ENTER WATERS OF THE STATE OF COLORADO, WHICH INCLUDES BUT ARE NOT LIMITED TO, SURFACE WATER, GROUND WATER, DRY GULLIES OR STORM SEWERS LEADING TO SURFACE WATER, SHALL BE IMMEDIATELY REPORTED TO THE COLORADO DEPARTMENT OF PUBLIC HEALTH AND ENVIRONMENT (CDPHE) PER 25-8-401, AND THE TOWN OF PARKER. RELEASES OF PETROLEUM PRODUCTS AND CERTAIN HAZARDOUS SUBSTANCES LISTED UNDER THE FEDERAL CLEAN WATER ACT (40 CFR PART 110) MUST BE REPORTED TO THE NATIONAL RESPONSE CENTER AND THE CDPEH. SPILLS THAT POSE AN IMMEDIATE SAFETY HAZARD SHALL BE REPORTED TO 911.
 26. THE CLEANING OF CONCRETE TRUCKS AND EQUIPMENT IS RESTRICTED TO THE APPROVED CONCRETE WASHOUT LOCATION ON THE JOB SITE. CONCRETE WASH WATER SHALL NOT BE DISCHARGED TO STATE WATERS OR STORM SEWER SYSTEMS.
 27. VEHICLE AND EQUIPMENT DEGREASING IS PROHIBITED ON THE JOB SITE.
 28. ALL DEWATERING ON SITE SHALL BE COORDINATED WITH THE TOWN'S INSPECTOR. A STATE PERMIT MAY BE REQUIRED FOR DEWATERING. THE EROSION CONTROL SUPERVISOR IS RESPONSIBLE FOR OBTAINING AND ADHERING TO ALL APPLICABLE PERMITS.
 29. HYDRAULIC SEEDING AND/OR HYDRAULIC MULCHING ARE ONLY ALLOWED IN AREAS UNDER TEMPORARY OR PERMANENT IRRIGATION OR FOR THE PURPOSE OF TEMPORARY SOIL STABILIZATION.
 30. APPLICABLE CONSTRUCTION BMPs SHALL REMAIN IN PLACE AND PROPERLY MAINTAINED UNTIL ALL LANDSCAPING HAS BEEN INSTALLED AND THE DESIRABLE VEGETATION HAS REACHED A POINT IN WHICH EROSION AND SEDIMENTATION IS NO LONGER A CONCERN AS DETERMINED BY THE TOWN'S INSPECTOR.
 31. GRADING SECURITY RELEASE REQUIREMENTS:
 - (i) DEVELOPABLE PROPERTY: IN ORDER FOR THE GRADING SECURITY TO BE RELEASED, THE SITE MUST MEET ITEMS A-H OR ITEM I (BELOW).
 - (ii) NONDEVELOPABLE PROPERTY: IN ORDER FOR THE GRADING SECURITY TO BE RELEASED, THE SITE MUST MEET ITEMS A-H AND J, OR ITEMS I AND J (BELOW).
- DEFINITIONS:**
 DEVELOPABLE PROPERTY MEANS ANY LAND THAT HAS BEEN GRADED AND IS PART OF A PLATTED LOT OR PLATTED TRACT OF RECORD, THAT WAS PLATTED FOR FUTURE DEVELOPMENT, INCLUDING PERMANENTLY CEASED, RESIDENTIAL HOME CONSTRUCTION OR PUBLIC IMPROVEMENTS.
 NONDEVELOPABLE PROPERTY MEANS LAND THAT HAS BEEN GRADED AND WILL NOT BE FURTHER DEVELOPED AS PART OF ANY FUTURE DEVELOPMENT. EXAMPLES INCLUDE, BUT ARE NOT LIMITED TO, PARKS, OPEN SPACE, HOMEOWNER ASSOCIATION OR BUSINESS ASSOCIATION PLATTED TRACTS, DETENTION PONDS AND DRAINAGEWAYS.
 FAILURE TO COMPLY WITH ANY OF THE REQUIREMENTS DESCRIBED IN THIS SECTION MAY RESULT IN THE ISSUANCE OF A NOTICE OF INTENT TO ISSUE A STOP WORK ORDER, A STOP WORK ORDER AND/OR THE REMEDIES/PENALTIES DESCRIBED IN CHAPTER 11.0 OF THE TOWN OF PARKER MUNICIPAL CODE.
 ANY PERSON CONVICTED OF VIOLATING ANY PROVISION OF THE TOWN OF PARKER, GRADING & EARTH MOVEMENT SECTION OF THE MUNICIPAL CODE SHALL BE GUILTY OF A MISDEMEANOR AND, UPON CONVICTION, BE PUNISHED BY A FINE OF NOT MORE THAN FOUR HUNDRED NINETY NINE DOLLARS (\$499.00) FOR EACH SEPARATE OFFENSE. EACH DAY A VIOLATION CONTINUES SHALL CONSTITUTE A SEPARATE OFFENSE. THE TOWN ALSO MAY SEEK IN MUNICIPAL COURT AN INJUNCTION, ABATEMENT, RESTITUTION OR ANY OTHER REMEDY TO PREVENT, ENJOIN, ABATE OR REMOVE THE VIOLATION. A PERSON CONVICTED OF VIOLATING CHAPTER 11.0 OF THE TOWN OF PARKER MUNICIPAL CODE SHALL BE LIABLE FOR THE ACTUAL COST OF REHABILITATING THE PROPERTY. THE COSTS MAY BE RECOVERED AS RESTITUTION IN MUNICIPAL COURT PROCEEDINGS OR IN A SEPARATE CIVIL ACTION.
 THE TOWN OF PARKER RESERVES THE RIGHT TO ALLOW MODIFICATIONS AND SUBSTITUTIONS TO THE CBMP NOTES AND DETAILS WHEN SUCH MODIFICATIONS AND SUBSTITUTIONS OFFER THE SAME LEVEL OF PROTECTION AS THE STANDARD REQUIREMENTS BASED UPON THE SPECIFIC SITUATION, AS DETERMINED BY TOWN STAFF. DUE TO THE INSIGNIFICANCE AND REGULARITY OF SUCH MODIFICATIONS AND SUBSTITUTIONS, THE APPROVAL OF SUCH VARIATIONS MAY NOT BE DOCUMENTED BY TOWN STAFF.

CBMP CONSTRUCTION BEST MANAGEMENT PRACTICES
 GEN NOTES 3 OF 4
 Oct. 2013

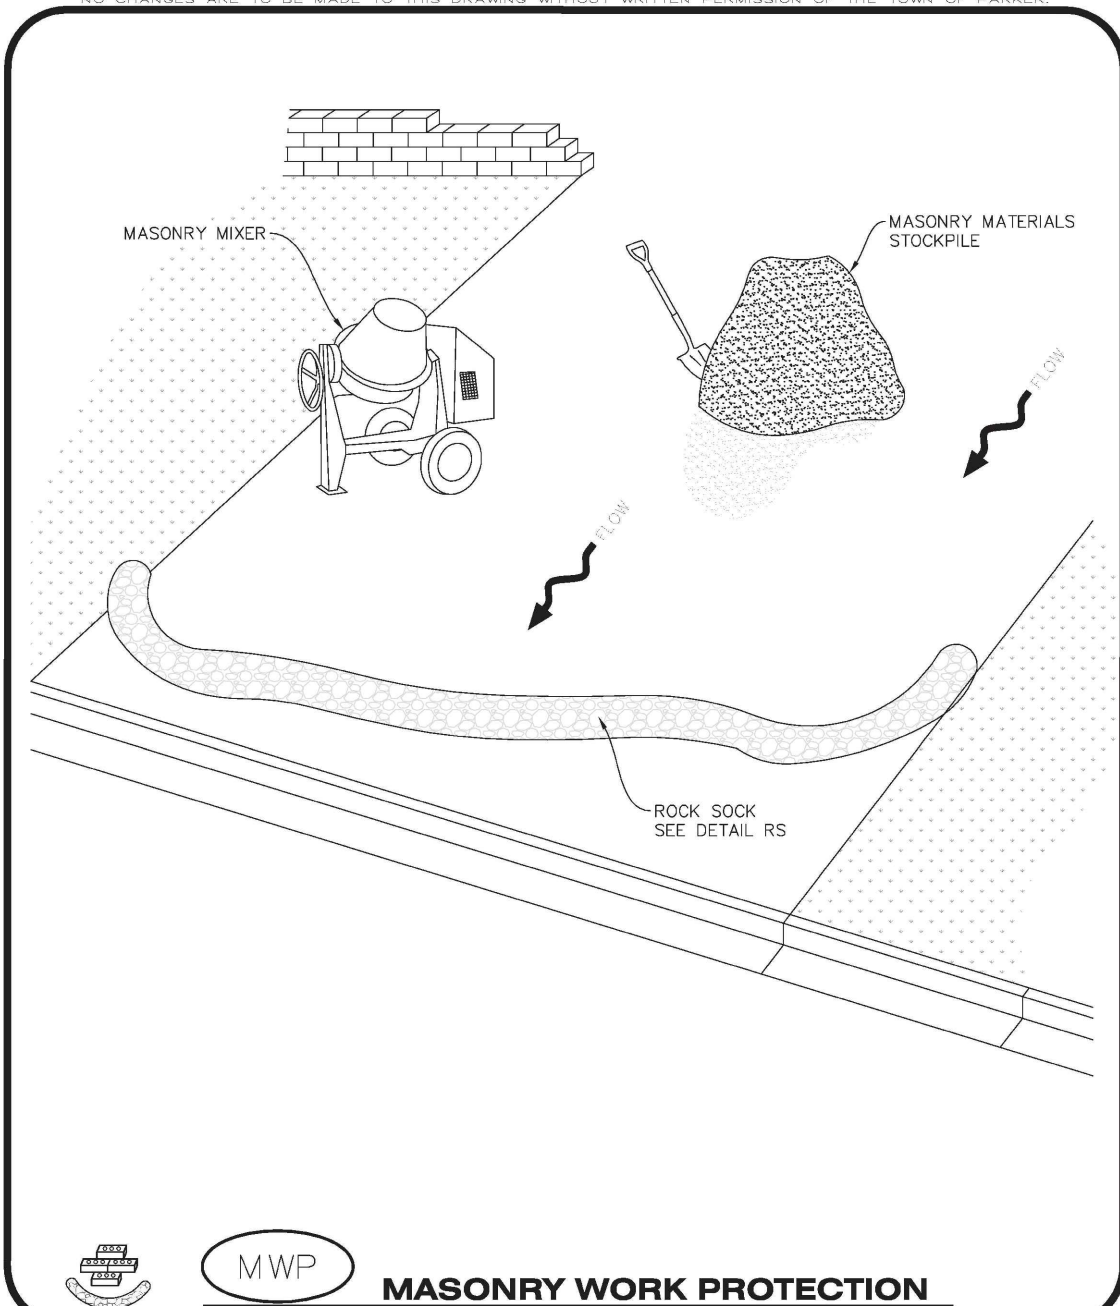

CBMP CONSTRUCTION BEST MANAGEMENT PRACTICES
 LEGEND MWP 1 OF 2
 Oct. 2013

- (i) DEVELOPABLE PROPERTY: IN ORDER FOR THE GRADING SECURITY TO BE RELEASED, THE SITE MUST MEET ITEMS A-H OR ITEM I (BELOW).
 - (ii) NONDEVELOPABLE PROPERTY: IN ORDER FOR THE GRADING SECURITY TO BE RELEASED, THE SITE MUST MEET ITEMS A-H AND J, OR ITEMS I AND J (BELOW).
- DEFINITIONS:**
 DEVELOPABLE PROPERTY MEANS ANY LAND THAT HAS BEEN GRADED AND IS PART OF A PLATTED LOT OR PLATTED TRACT OF RECORD, THAT WAS PLATTED FOR FUTURE DEVELOPMENT, INCLUDING PERMANENTLY CEASED, RESIDENTIAL HOME CONSTRUCTION OR PUBLIC IMPROVEMENTS.
 NONDEVELOPABLE PROPERTY MEANS LAND THAT HAS BEEN GRADED AND WILL NOT BE FURTHER DEVELOPED AS PART OF ANY FUTURE DEVELOPMENT. EXAMPLES INCLUDE, BUT ARE NOT LIMITED TO, PARKS, OPEN SPACE, HOMEOWNER ASSOCIATION OR BUSINESS ASSOCIATION PLATTED TRACTS, DETENTION PONDS AND DRAINAGEWAYS.
 FAILURE TO COMPLY WITH ANY OF THE REQUIREMENTS DESCRIBED IN THIS SECTION MAY RESULT IN THE ISSUANCE OF A NOTICE OF INTENT TO ISSUE A STOP WORK ORDER, A STOP WORK ORDER AND/OR THE REMEDIES/PENALTIES DESCRIBED IN CHAPTER 11.0 OF THE TOWN OF PARKER MUNICIPAL CODE.
 ANY PERSON CONVICTED OF VIOLATING ANY PROVISION OF THE TOWN OF PARKER, GRADING & EARTH MOVEMENT SECTION OF THE MUNICIPAL CODE SHALL BE GUILTY OF A MISDEMEANOR AND, UPON CONVICTION, BE PUNISHED BY A FINE OF NOT MORE THAN FOUR HUNDRED NINETY NINE DOLLARS (\$499.00) FOR EACH SEPARATE OFFENSE. EACH DAY A VIOLATION CONTINUES SHALL CONSTITUTE A SEPARATE OFFENSE. THE TOWN ALSO MAY SEEK IN MUNICIPAL COURT AN INJUNCTION, ABATEMENT, RESTITUTION OR ANY OTHER REMEDY TO PREVENT, ENJOIN, ABATE OR REMOVE THE VIOLATION. A PERSON CONVICTED OF VIOLATING CHAPTER 11.0 OF THE TOWN OF PARKER MUNICIPAL CODE SHALL BE LIABLE FOR THE ACTUAL COST OF REHABILITATING THE PROPERTY. THE COSTS MAY BE RECOVERED AS RESTITUTION IN MUNICIPAL COURT PROCEEDINGS OR IN A SEPARATE CIVIL ACTION.
 THE TOWN OF PARKER RESERVES THE RIGHT TO ALLOW MODIFICATIONS AND SUBSTITUTIONS TO THE CBMP NOTES AND DETAILS WHEN SUCH MODIFICATIONS AND SUBSTITUTIONS OFFER THE SAME LEVEL OF PROTECTION AS THE STANDARD REQUIREMENTS BASED UPON THE SPECIFIC SITUATION, AS DETERMINED BY TOWN STAFF. DUE TO THE INSIGNIFICANCE AND REGULARITY OF SUCH MODIFICATIONS AND SUBSTITUTIONS, THE APPROVAL OF SUCH VARIATIONS MAY NOT BE DOCUMENTED BY TOWN STAFF.

CBMP CONSTRUCTION BEST MANAGEMENT PRACTICES
 GEN NOTES 4 OF 4
 Oct. 2013

- MASONRY WORK PROTECTION INSTALLATION NOTES**
1. MASONRY WORK PROTECTION MAY NEED TO BE INSTALLED WHEN MASONRY WORK AND MIXING IS OCCURRING.
 2. A ROCK SOCK SHALL BE INSTALLED IN A CRESCENT SHAPE ON THE DOWNHILL SIDE OF THE MASONRY WORK AND MIXER.
 3. CRUSHED ROCK SHALL BE 2.0"-3.0" IN SIZE WITH A FRACTURED FACE (ALL SIDES).
 4. ROCK SOCK SHALL BE ONE CONTINUOUS PIECE OR SHALL BE CONSTRUCTED USING WIRE WRAPPED JOINTS (SEE DETAIL RS).
 5. ROCK SOCK SHALL BE CONSTRUCTED USING CHICKEN WIRE OR OTHER APPROVED MATERIAL, SIZED TO KEEP ROCK FROM SPILLING OUT.
- MASONRY WORK PROTECTION INSPECTION AND MAINTENANCE NOTES**
1. THE EROSION CONTROL SUPERVISOR SHALL REGULARLY INSPECT THE MASONRY WORK PROTECTION.
 2. ALL CONCRETE WASTE SHALL BE REGULARLY CLEANED AND PLACED IN THE CONCRETE WASH OUT AREA.
 3. ROCK SOCKS SHALL BE REPLACED IF THEY BECOME HEAVILY SOILED OR DAMAGED.

CBMP CONSTRUCTION BEST MANAGEMENT PRACTICES
 LEGEND MWP 2 OF 2
 Oct. 2013

- CD CHECK DAM
- CF CONSTRUCTION FENCE
- CP CULVERT PROTECTION
- CWA CONCRETE WASHOUT AREA
- D DEWATERING
- DD DIVERSION DITCH
- DP DETENTION POND PROTECTION
- DTC DEBRIS TRASH CONTROL
- ECB EROSION CONTROL BLANKET
- IPAN INLET PROTECTION FOR AREA INLETS NOT IN PAVEMENT
- IPAP INLET PROTECTION FOR AREA INLETS IN PAVEMENT
- IPCOG INLET PROTECTION, CURB ON-GRADE, TYPE R INLET
- IPCOS INLET PROTECTION, CURB ON SUMP, TYPE R INLET


CBMP CONSTRUCTION BEST MANAGEMENT PRACTICES
 LEGEND 1 OF 3
 Oct. 2013

Add Parker's COMPLETE List of Keys/Symbols (1st), General Notes (2nd), and Erosion Control Details in ALPHABETICAL Order (3rd), Immediately Following the Final Erosion Control Plan Sheet.

CALL UNCC
 TWO WORKING DAYS
 BEFORE YOU DIG
 CALL 811
 METRO DENVER AREA
 UTILITY NOTIFICATION CENTER OF COLORADO


ENGINEER'S STATEMENT
 PREPARED UNDER MY SUPERVISION

BRIAN KROMBEIN, PE, PLS DATE
 COLORADO PE NO. 34294
 FOR AND ON BEHALF OF
 VERMILION PEAK ENGINEERING LLC



UNTIL SUCH TIME AS THESE DRAWINGS ARE APPROVED BY THE APPROPRIATE VERMILION PE OFFICES, THESE DRAWINGS ARE NOT TO BE USED FOR ANY PURPOSES DESIGNATED BY WRITTEN AUTHORIZATION.

PREPARED FOR
 VENTANA CAPITAL
 8678 CONCORD CENTER DR, SUITE 200
 ENGLEWOOD, CO 80112
 720-703-9036
 CONTACT: DALTON HORAN



H-SCALE	AS SHOWN	NO.	REVISION	BY	DATE
V-SCALE	2/12/25				
DESIGNED BY	BK				
DRAWN BY	BK				
CHECKED BY					

HORSE CREEK COMMERCIAL
 EROSION CONTROL DETAILS

SHEET C8 OF 17
 JOB NO. 24020
